


Date: **Monday 26 Oct 2020**

BSUoS Charge Estimate: £4.27/MWh





Total Outturn: £5.71m

BM Cost (Indicative)

AS Cost (Estimate)



Daily Balancing Costs

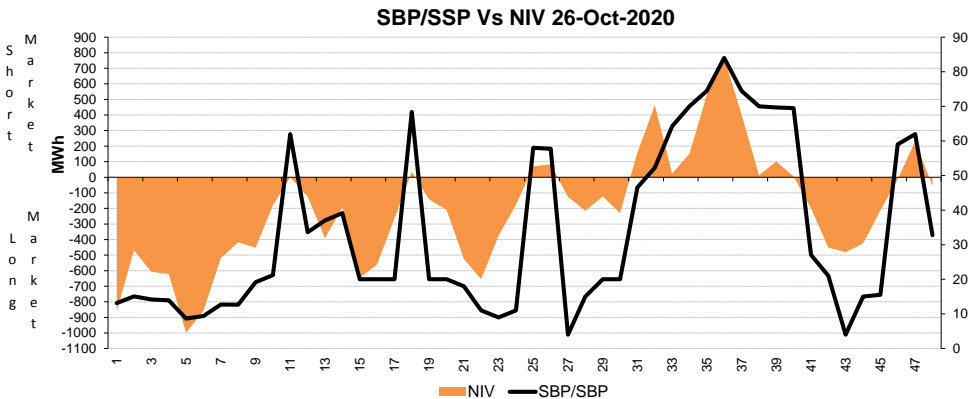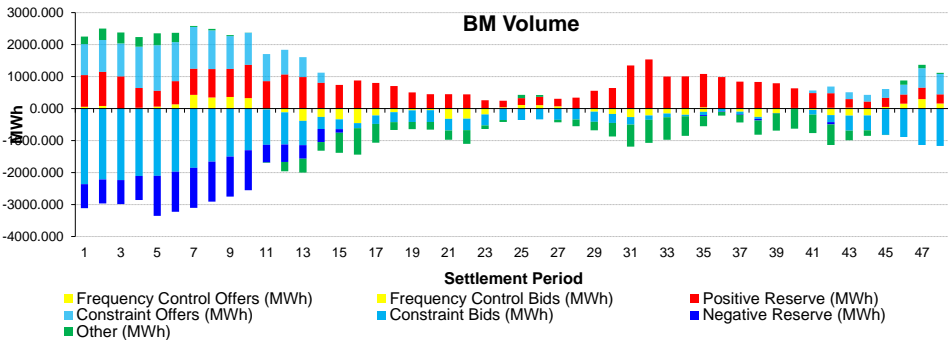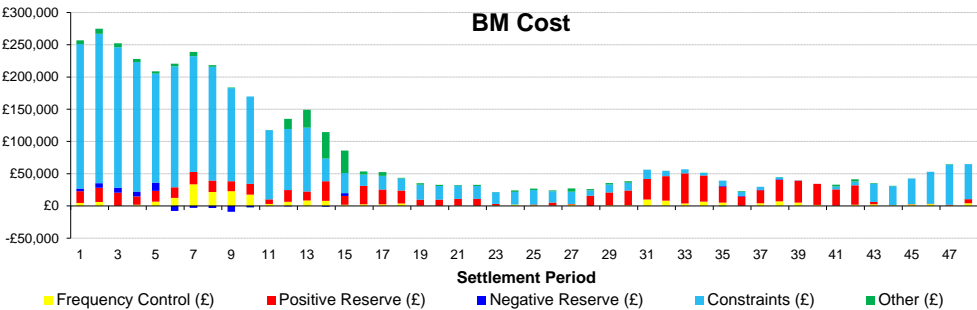

Western Link status: Available

Commentary

The market was mostly long up to midday and mostly short thereafter. Interconnector trades were enacted to create downward margin for the early morning period up to 6am and interconnector trades were made for margin during the afternoon peak.

The Western Link HVDC circuit returned to bipolar configuration with a 2250MW capability at 23.45 hours following its trip on Sunday morning.

BM Actions were used to manage constraints in Scotland during the early morning period, and BM Actions were needed to provide voltage support & manage RoCoF in the early morning period.

Trades and BM Actions were carried out to manage RoCoF for the overnight period.
