ID	Task Name	Duration	Resource Names
1	Extract Outturn Intertia	0.5 hrs	Individual
2	Extract Frequency Data (Data Historian)	2 hrs	Individual
3	Extract BMU Data (Data Historian)	4 hrs	Individual
4	Data Check & Running of R codes to find BMU MW Change	1 hr	Individual
5	Data Check & Running of R codes to find RoCoF	1 hr	Individual
6	Comparing R code results (Excel)	1.5 hrs	Individual
7	Produce a list of possible events	2 hrs	Individual
8	Investigate list of possible events 1 by 1	1 hr	Joint
9	Finalise report draft	1 hr	Individual
10	Check control room daily reports and identify missing events	1 hr	Individual
11	Request data from TOs	0 hrs	Individual
12	Wait for TO data	2.5 hrs	Wait
13	Investigate TO received d	1.5 hrs	Joint
14	Final review & report che	4 hrs	Individual
15	Manager Approval	2 hrs	Individual
16	Upload file to website and approve	2 hrs	Individual

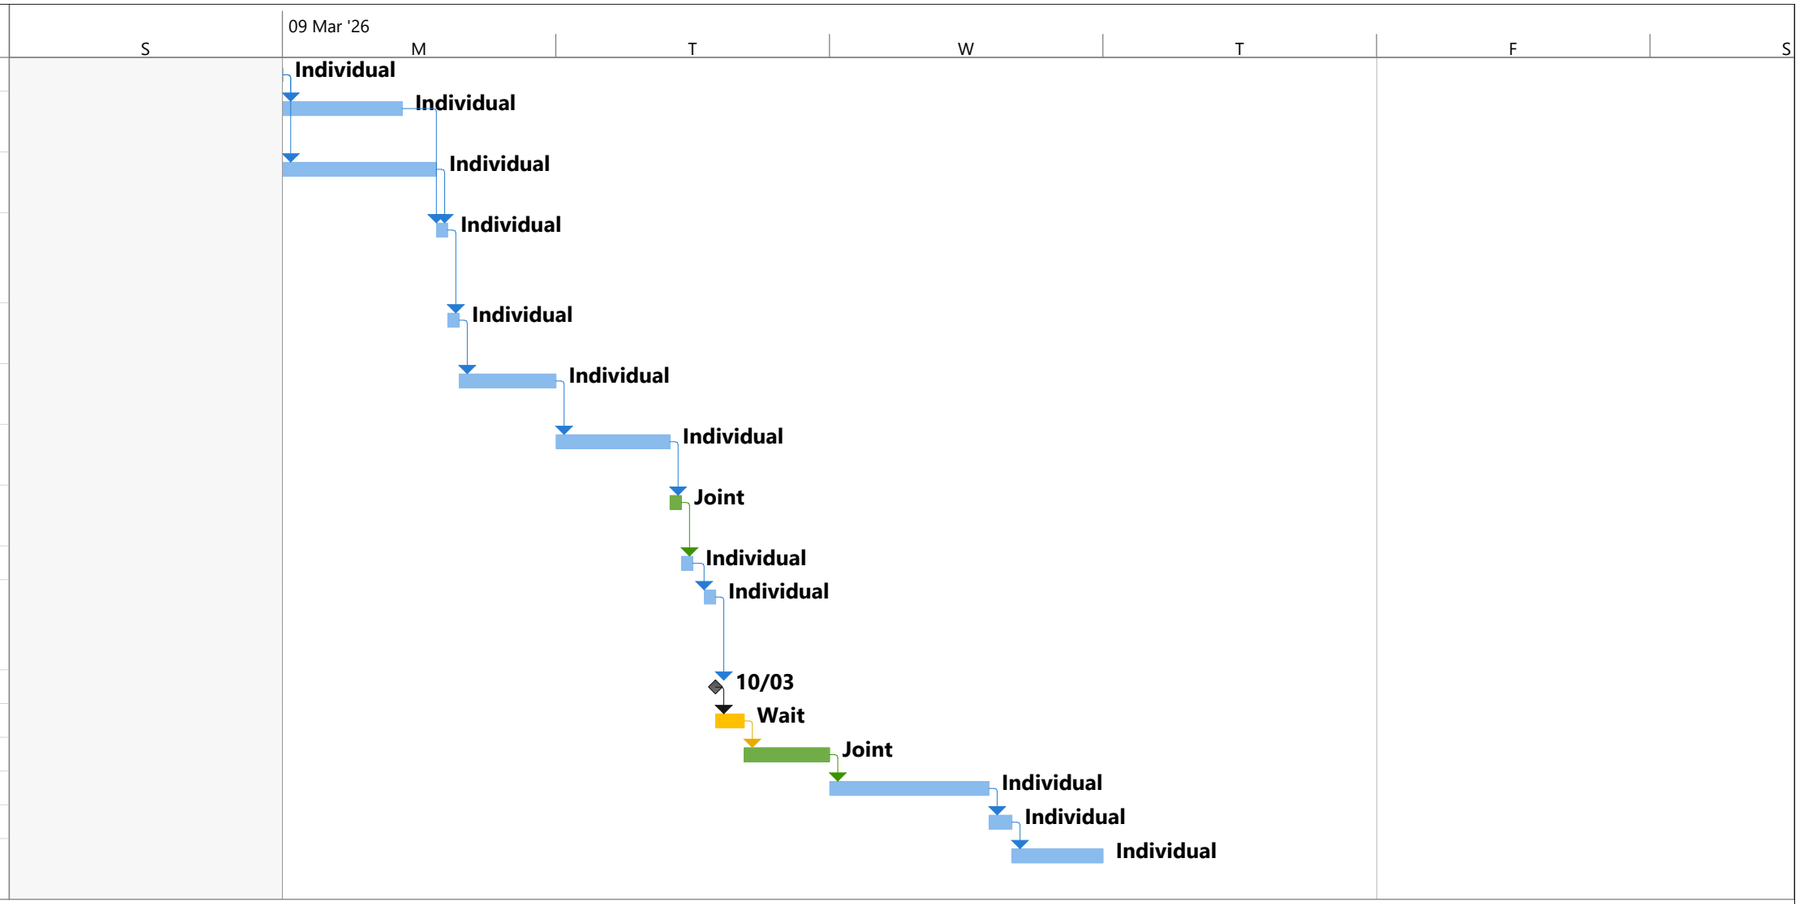

Project: GC0181 - Weekly, Extra
Date: Tue 17/03/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone
